
ACTIVITY ID	ACTIVITY NAME	AT COMPL. DURATION	START	FINISH
Mountain Ridge Elementary School				
Key Milestones				
MS1020	Classroom Building Dry-In Milestone	0d	26-Aug-26	26-Aug-26
Sitework				
Bus Loop, Parking and Playfields				
ST1160	Install Irrigation and Landscaping	20d	08-Jul-26A	04-Aug-26
ST1150	Install Playground Equipment and Surfacing	10d	23-Jul-26A	05-Aug-26
Classroom Building				
Envelope				
CB1140	Install Roofing System - Classroom Building	16d	17-Jul-26A	07-Aug-26
CB1160	Install Air Barrier and Sealants - Classroom Building	12d	29-Jul-26A	13-Aug-26
CB1150	Install Windows and Curtain Wall - Classroom Building	21d	29-Jul-26A	26-Aug-26
CB1180	Apply Exterior Stucco and Paint - Classroom Building	25d	14-Aug-26	18-Sep-26
CB1170	Classroom Building Dry-In	0d	26-Aug-26	26-Aug-26
Interiors				
Level 1 East Wing				
L1E1000	Layout and Frame Interior Walls - Level 1 East Wing	10d	27-Aug-26	10-Sep-26
L1E1010	Install Overhead Plumbing - Level 1 East Wing	8d	11-Sep-26	22-Sep-26
L1E1030	Install Overhead Fire Sprinkler Piping - Level 1 East Wing	8d	11-Sep-26	22-Sep-26
L1E1020	Install Overhead HVAC Ductwork - Level 1 East Wing	10d	11-Sep-26	24-Sep-26
L1E1040	Install Overhead Electrical and Data Conduit - Level 1 East Wing	10d	11-Sep-26	24-Sep-26
Level 1 West Wing				
L1W1000	Layout and Frame Interior Walls - Level 1 West Wing	10d	11-Sep-26	24-Sep-26
Vertical Transportation and Systems				
CB1210	Set Rooftop Air Handling Units - Classroom Building	5d	10-Aug-26	14-Aug-26
CB1230	Set Main Switchgear and Panelboards - Classroom Building	5d	27-Aug-26	02-Sep-26
CB1200	Install Elevator - Classroom Building	25d	27-Aug-26	01-Oct-26
CB1240	Connect Permanent Power - Classroom Building	3d	03-Sep-26	08-Sep-26
CB1250	Install Fire Alarm and Intercom Head-End - Classroom Building	8d	03-Sep-26	15-Sep-26
CB1260	Start Up HVAC and Test and Balance - Classroom Building	15d	09-Sep-26	29-Sep-26
Core Building (Admin, Cafeteria, Media)				
Shell				
KB1040	Lay Load-Bearing CMU Walls - Core Building	20d	09-Jul-26A	05-Aug-26
KB1050	Form and Pour Bond Beams - Core Building	6d	06-Aug-26	13-Aug-26
KB1060	Erect Steel Framing at Cafeteria - Core Building	8d	14-Aug-26	25-Aug-26
KB1070	Set Roof Joists and Deck - Core Building	8d	26-Aug-26	04-Sep-26
KB1090	Install Storefront and Windows - Core Building	12d	27-Aug-26	14-Sep-26
KB1080	Install Roofing System - Core Building	12d	08-Sep-26	23-Sep-26
Time Impacts				
OD-02 Covered Walkway				
TI1140	Install Covered Walkway Foundations	5d	30-Jul-26A	05-Aug-26
TI1130	Fabricate Covered Walkway Canopy	32d	30-Jul-26A	14-Sep-26

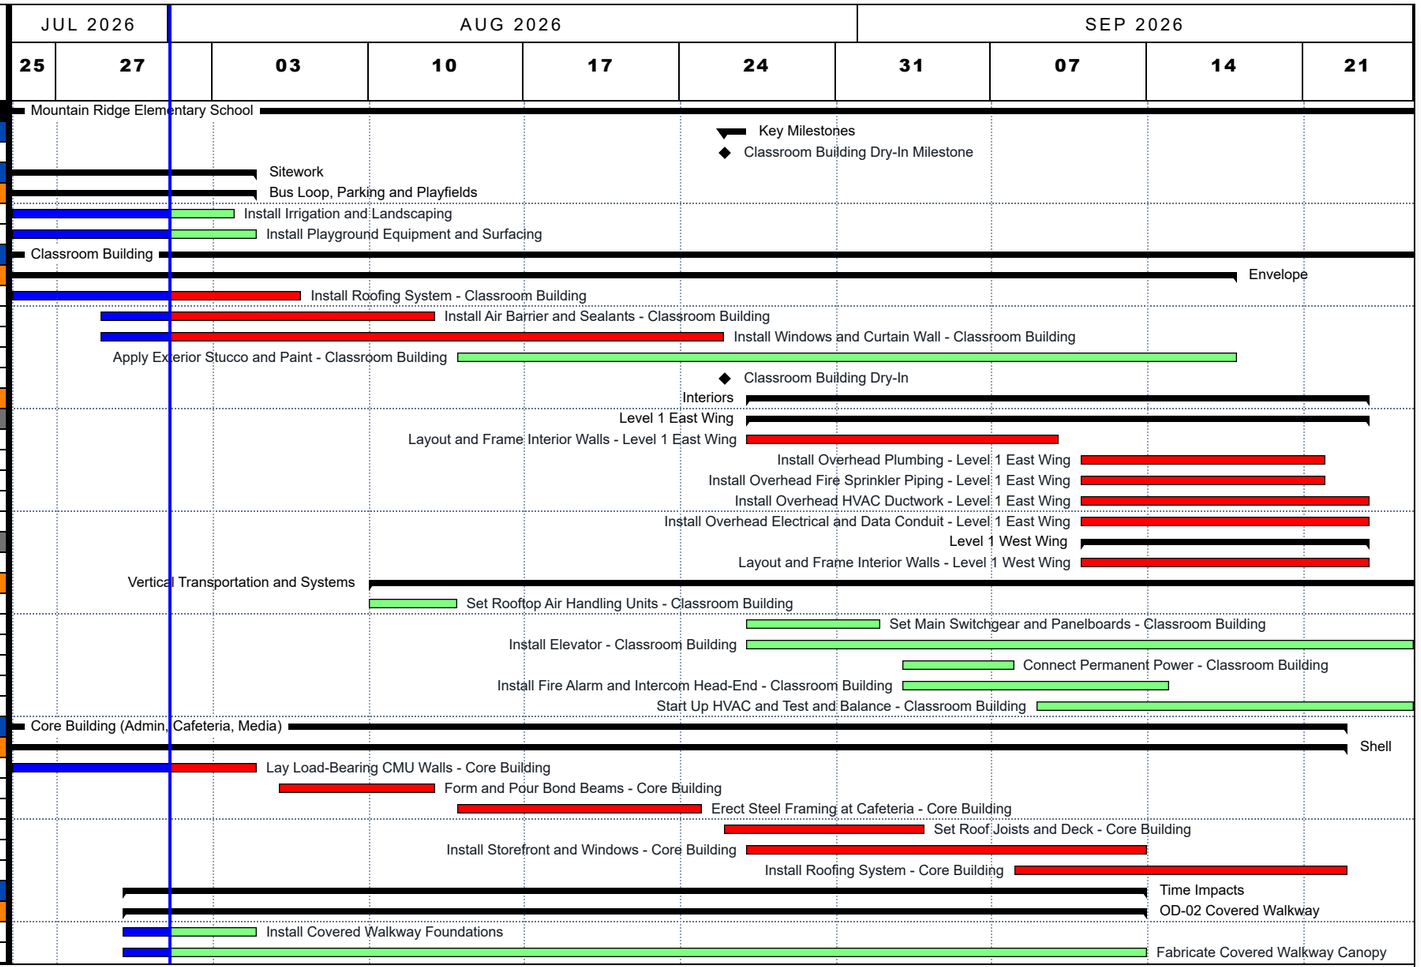

LEGEND

- Critical remaining
- Actual work
- Milestone
- Remaining
- Summary

Mountain Ridge Elementary School

All Activities · 6WLA Report

ORGANIZATION	Sample Builders
DATA DATE	01-Aug-26
TURNOVER	All Activities
LAYOUT	6WLA Report
