
ACTIVITY ID	ACTIVITY NAME	AT COMPL. DURATION	START	FINISH	TOTAL FLOAT (CD)
MS1020 · Classroom Building Dry-In Milestone					
Float Path 1					
CB1150	Install Windows and Curtain Wall - Classroom Building	21d	29-Jul-26A	26-Aug-26	**-35 CD**
CB1170	Classroom Building Dry-In	0d	26-Aug-26	26-Aug-26	**-35 CD**
MS1020	Classroom Building Dry-In Milestone	0d	26-Aug-26	26-Aug-26	**-21 CD**
Float Path 2					
CB1160	Install Air Barrier and Sealants - Classroom Building	12d	29-Jul-26A	13-Aug-26	**-22 CD**
CB1170	Classroom Building Dry-In	0d	26-Aug-26	26-Aug-26	**-35 CD**
MS1020	Classroom Building Dry-In Milestone	0d	26-Aug-26	26-Aug-26	**-21 CD**
Float Path 3					
CB1140	Install Roofing System - Classroom Building	16d	17-Jul-26A	07-Aug-26	**-16 CD**
CB1170	Classroom Building Dry-In	0d	26-Aug-26	26-Aug-26	**-35 CD**
MS1020	Classroom Building Dry-In Milestone	0d	26-Aug-26	26-Aug-26	**-21 CD**

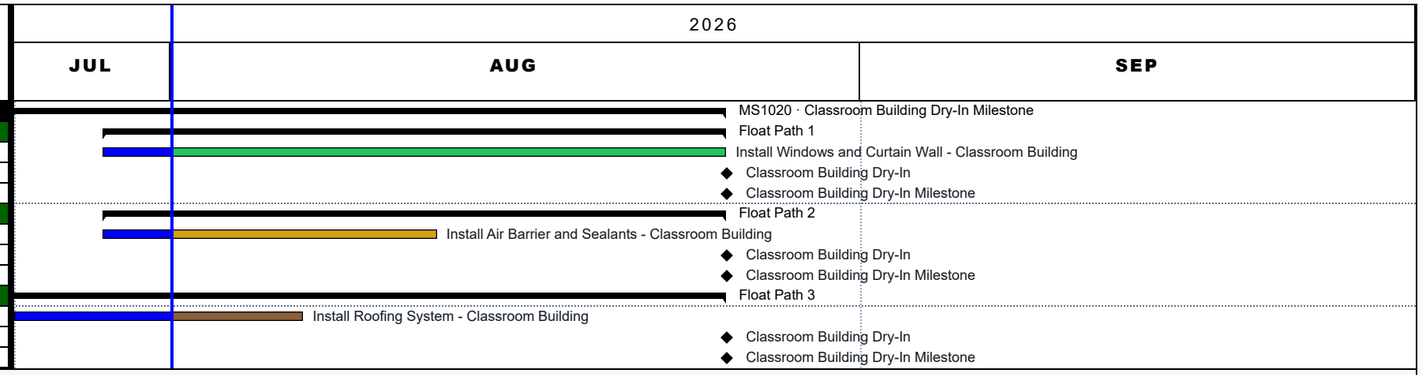

LEGEND

- Path 1
- Path 2
- Path 3
- Actual work
- Summary
- Milestone

Mountain Ridge Elementary School

Classroom Building Dry-In Milestone · Phase Path Report

ORGANIZATION	Sample Builders
DATA DATE	01-Aug-26
TURNOVER	Classroom Building Dry-In Milestone
LAYOUT	Phase Path Report
