
ACTIVITY ID	ACTIVITY NAME	AT COMPL. DURATION	START	FINISH	TOTAL FLOAT (CD)
MS1030 · Core Building Dry-In Milestone					
Float Path 1					
KB1040	Lay Load-Bearing CMU Walls - Core Building	20d	09-Jul-26A	05-Aug-26	**-21 CD**
KB1050	Form and Pour Bond Beams - Core Building	6d	06-Aug-26	13-Aug-26	**-21 CD**
KB1060	Erect Steel Framing at Cafeteria - Core Building	8d	14-Aug-26	25-Aug-26	**-21 CD**
KB1070	Set Roof Joists and Deck - Core Building	8d	26-Aug-26	04-Sep-26	**-21 CD**
KB1080	Install Roofing System - Core Building	12d	08-Sep-26	23-Sep-26	**-22 CD**
KB1100	Core Building Dry-In	0d	23-Sep-26	23-Sep-26	**-22 CD**
MS1030	Core Building Dry-In Milestone	0d	23-Sep-26	23-Sep-26	**-22 CD**
Float Path 2					
CB1150	Install Windows and Curtain Wall - Classroom Building	21d	29-Jul-26A	26-Aug-26	**-35 CD**
KB1090	Install Storefront and Windows - Core Building	12d	27-Aug-26	14-Sep-26	**-13 CD**
KB1100	Core Building Dry-In	0d	23-Sep-26	23-Sep-26	**-22 CD**
MS1030	Core Building Dry-In Milestone	0d	23-Sep-26	23-Sep-26	**-22 CD**
Float Path 3					
CB1140	Install Roofing System - Classroom Building	16d	17-Jul-26A	07-Aug-26	**-16 CD**
KB1080	Install Roofing System - Core Building	12d	08-Sep-26	23-Sep-26	**-22 CD**
KB1100	Core Building Dry-In	0d	23-Sep-26	23-Sep-26	**-22 CD**
MS1030	Core Building Dry-In Milestone	0d	23-Sep-26	23-Sep-26	**-22 CD**

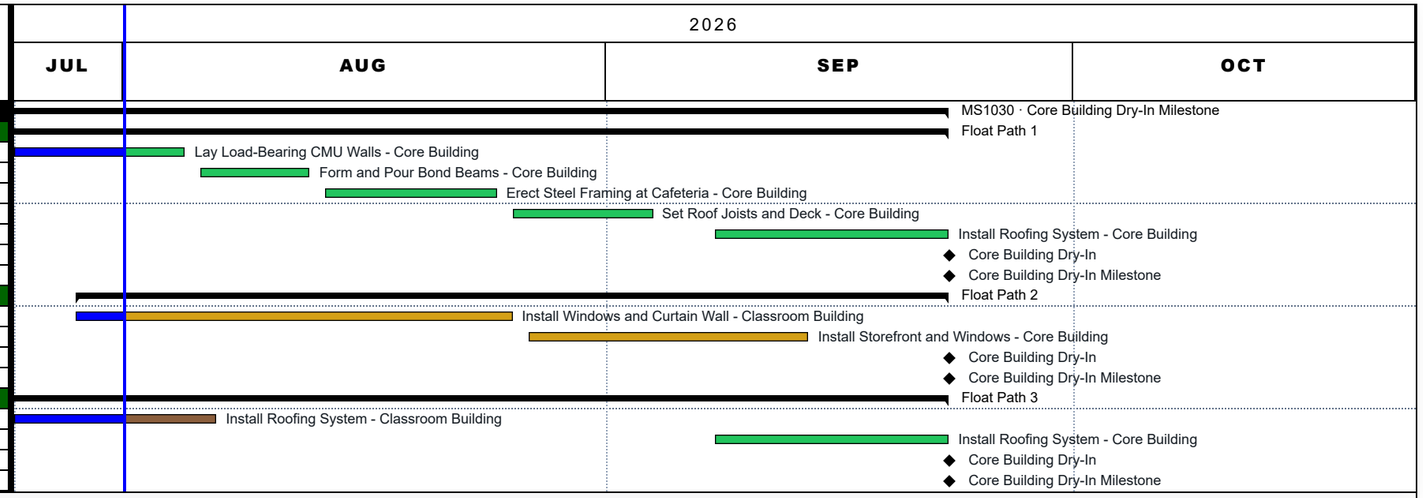

LEGEND

- Path 1
- Path 2
- Path 3
- Actual work
- Summary
- Milestone

Mountain Ridge Elementary School

Core Building Dry-In Milestone · Phase Path Report

ORGANIZATION	Sample Builders
DATA DATE	01-Aug-26
TURNOVER	Core Building Dry-In Milestone
LAYOUT	Phase Path Report
