
ACTIVITY ID	ACTIVITY NAME	AT COMPL. DURATION	START	FINISH	TOTAL FLOAT (CD)
MS1040 · Substantial Completion					
Float Path 1					
CB1150	Install Windows and Curtain Wall - Classroom Building	21d	29-Jul-26A	26-Aug-26	**-35 CD**
CB1170	Classroom Building Dry-In	0d	26-Aug-26	26-Aug-26	**-35 CD**
L1E1000	Layout and Frame Interior Walls - Level 1 East Wing	10d	27-Aug-26	10-Sep-26	**-36 CD**
L1W1000	Layout and Frame Interior Walls - Level 1 West Wing	10d	11-Sep-26	24-Sep-26	**-36 CD**
L2W1000	Layout and Frame Interior Walls - Level 2 West Wing	10d	25-Sep-26	08-Oct-26	**-36 CD**
L2E1000	Layout and Frame Interior Walls - Level 2 East Wing	10d	09-Oct-26	22-Oct-26	**-35 CD**
L2E1040	Install Overhead Electrical and Data Conduit - Level 2 East Wing	10d	23-Oct-26	05-Nov-26	**-35 CD**
L2E1050	Install In-Wall MEP Rough-In - Level 2 East Wing	8d	06-Nov-26	17-Nov-26	**-35 CD**
L2E1060	MEP Rough-In Inspections - Level 2 East Wing	3d	18-Nov-26	20-Nov-26	**-35 CD**
L2E1070	Insulate and Hang Drywall - Level 2 East Wing	10d	23-Nov-26	08-Dec-26	**-39 CD**
L2E1080	Tape and Finish Drywall - Level 2 East Wing	10d	09-Dec-26	22-Dec-26	**-39 CD**
L2W1070	Insulate and Hang Drywall - Level 2 West Wing	10d	09-Dec-26	22-Dec-26	**-39 CD**
L2W1080	Tape and Finish Drywall - Level 2 West Wing	10d	23-Dec-26	11-Jan-27	**-41 CD**
L2W1090	Prime and First Coat Paint - Level 2 West Wing	6d	12-Jan-27	19-Jan-27	**-41 CD**
L2W1100	Install Ceiling Grid - Level 2 West Wing	6d	20-Jan-27	27-Jan-27	**-41 CD**
L2W1110	Above-Ceiling Inspection - Level 2 West Wing	2d	28-Jan-27	29-Jan-27	**-39 CD**
L2W1120	Install Ceiling Devices and Light Fixtures - Level 2 West Wing	8d	01-Feb-27	10-Feb-27	**-35 CD**
L2W1130	Install Ceiling Tile - Level 2 West Wing	5d	11-Feb-27	17-Feb-27	**-35 CD**
L2W1150	Install Resilient Flooring and Base - Level 2 West Wing	8d	18-Feb-27	01-Mar-27	**-35 CD**
L2W1160	Hang Doors and Install Hardware - Level 2 West Wing	6d	02-Mar-27	09-Mar-27	**-35 CD**
L2W1180	Final Paint and Touch-Up - Level 2 West Wing	4d	10-Mar-27	15-Mar-27	**-35 CD**
L2W1190	Final Clean and Punch List - Level 2 West Wing	5d	16-Mar-27	22-Mar-27	**-35 CD**
CL1000	Fire Alarm Acceptance Test	3d	23-Mar-27	25-Mar-27	**-35 CD**
CL1030	Fire Marshal Final Inspection	3d	26-Mar-27	30-Mar-27	**-35 CD**
MS1040	Substantial Completion	0d	30-Mar-27	30-Mar-27	**-35 CD**
Float Path 2					
L2W1170	Install Markerboards, Tackboards and Specialties - Level 2 West Wing	5d	02-Mar-27	08-Mar-27	**-34 CD**
L2W1180	Final Paint and Touch-Up - Level 2 West Wing	4d	10-Mar-27	15-Mar-27	**-35 CD**
L2W1190	Final Clean and Punch List - Level 2 West Wing	5d	16-Mar-27	22-Mar-27	**-35 CD**
CL1000	Fire Alarm Acceptance Test	3d	23-Mar-27	25-Mar-27	**-35 CD**
CL1030	Fire Marshal Final Inspection	3d	26-Mar-27	30-Mar-27	**-35 CD**
MS1040	Substantial Completion	0d	30-Mar-27	30-Mar-27	**-35 CD**
Float Path 3					
L2E1010	Install Overhead Plumbing - Level 2 East Wing	8d	23-Oct-26	03-Nov-26	**-33 CD**
L2E1050	Install In-Wall MEP Rough-In - Level 2 East Wing	8d	06-Nov-26	17-Nov-26	**-35 CD**
L2E1060	MEP Rough-In Inspections - Level 2 East Wing	3d	18-Nov-26	20-Nov-26	**-35 CD**
L2E1070	Insulate and Hang Drywall - Level 2 East Wing	10d	23-Nov-26	08-Dec-26	**-39 CD**
L2E1080	Tape and Finish Drywall - Level 2 East Wing	10d	09-Dec-26	22-Dec-26	**-39 CD**
L2W1080	Tape and Finish Drywall - Level 2 West Wing	10d	23-Dec-26	11-Jan-27	**-41 CD**
L2W1090	Prime and First Coat Paint - Level 2 West Wing	6d	12-Jan-27	19-Jan-27	**-41 CD**
L2W1100	Install Ceiling Grid - Level 2 West Wing	6d	20-Jan-27	27-Jan-27	**-41 CD**
L2W1110	Above-Ceiling Inspection - Level 2 West Wing	2d	28-Jan-27	29-Jan-27	**-39 CD**
L2W1120	Install Ceiling Devices and Light Fixtures - Level 2 West Wing	8d	01-Feb-27	10-Feb-27	**-35 CD**
L2W1130	Install Ceiling Tile - Level 2 West Wing	5d	11-Feb-27	17-Feb-27	**-35 CD**
L2W1150	Install Resilient Flooring and Base - Level 2 West Wing	8d	18-Feb-27	01-Mar-27	**-35 CD**
L2W1160	Hang Doors and Install Hardware - Level 2 West Wing	6d	02-Mar-27	09-Mar-27	**-35 CD**
L2W1180	Final Paint and Touch-Up - Level 2 West Wing	4d	10-Mar-27	15-Mar-27	**-35 CD**
L2W1190	Final Clean and Punch List - Level 2 West Wing	5d	16-Mar-27	22-Mar-27	**-35 CD**
CL1000	Fire Alarm Acceptance Test	3d	23-Mar-27	25-Mar-27	**-35 CD**
CL1030	Fire Marshal Final Inspection	3d	26-Mar-27	30-Mar-27	**-35 CD**
MS1040	Substantial Completion	0d	30-Mar-27	30-Mar-27	**-35 CD**
Float Path 4					
L2E1090	Prime and First Coat Paint - Level 2 East Wing	6d	23-Dec-26	05-Jan-27	**-41 CD**
L2E1100	Install Ceiling Grid - Level 2 East Wing	6d	06-Jan-27	13-Jan-27	**-37 CD**
L2E1110	Above-Ceiling Inspection - Level 2 East Wing	2d	14-Jan-27	15-Jan-27	**-37 CD**
L2E1120	Install Ceiling Devices and Light Fixtures - Level 2 East Wing	8d	18-Jan-27	27-Jan-27	**-37 CD**
L2E1130	Install Ceiling Tile - Level 2 East Wing	5d	28-Jan-27	03-Feb-27	**-35 CD**
L2E1150	Install Resilient Flooring and Base - Level 2 East Wing	8d	04-Feb-27	15-Feb-27	**-33 CD**

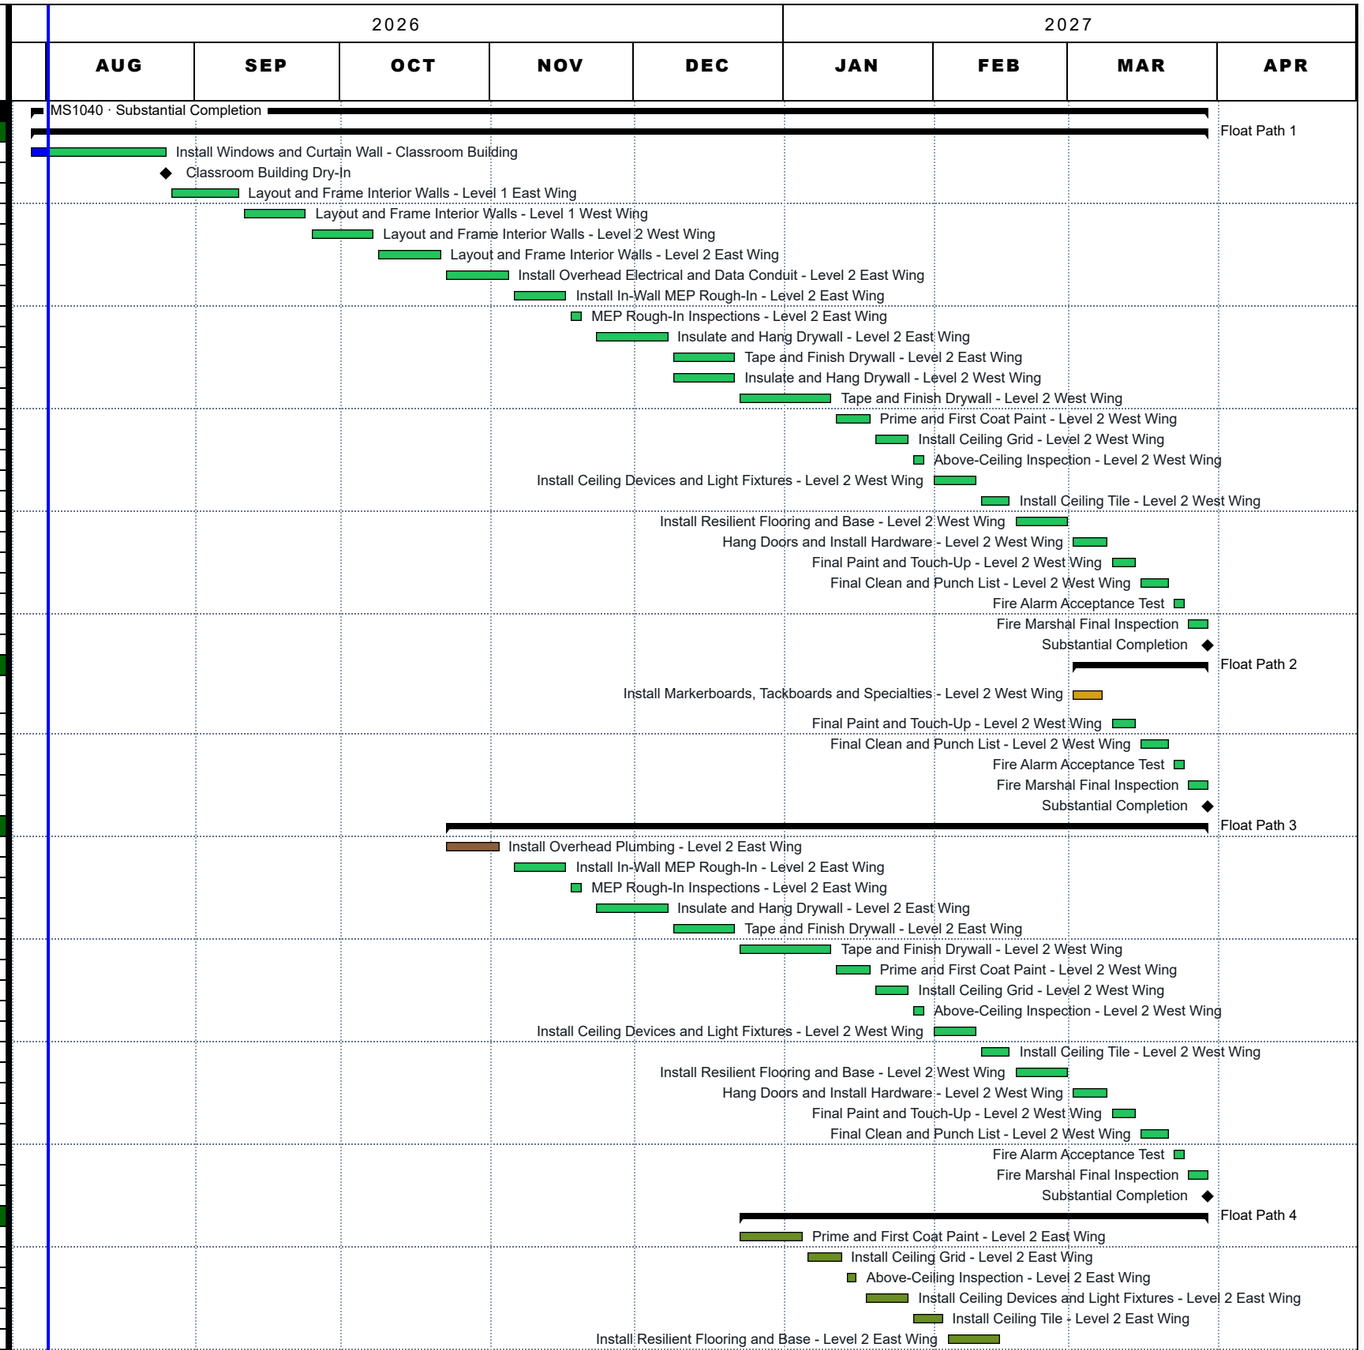

LEGEND


- Path 1
- Path 2
- Path 3
- Path 4
- Actual work
- Summary
- Milestone

Mountain Ridge Elementary School

Substantial Completion · Phase Path Report

ORGANIZATION	Sample Builders
DATA DATE	01-Aug-26
TURNOVER	Substantial Completion
LAYOUT	Phase Path Report

ACTIVITY ID	ACTIVITY NAME	AT COMPL. DURATION	START	FINISH	TOTAL FLOAT (CD)
MS1040 · Substantial Completion					
Float Path 4 · continued					
L2W1150	Install Resilient Flooring and Base - Level 2 West Wing	8d	18-Feb-27	01-Mar-27	**-35 CD**
L2W1160	Hang Doors and Install Hardware - Level 2 West Wing	6d	02-Mar-27	09-Mar-27	**-35 CD**
L2W1180	Final Paint and Touch-Up - Level 2 West Wing	4d	10-Mar-27	15-Mar-27	**-35 CD**
L2W1190	Final Clean and Punch List - Level 2 West Wing	5d	16-Mar-27	22-Mar-27	**-35 CD**
CL1000	Fire Alarm Acceptance Test	3d	23-Mar-27	25-Mar-27	**-35 CD**
CL1030	Fire Marshal Final Inspection	3d	26-Mar-27	30-Mar-27	**-35 CD**
MS1040	Substantial Completion	0d	30-Mar-27	30-Mar-27	**-35 CD**
Float Path 5					
L2E1020	Install Overhead HVAC Ductwork - Level 2 East Wing	10d	23-Oct-26	05-Nov-26	**-23 CD**
L2E1060	MEP Rough-In Inspections - Level 2 East Wing	3d	18-Nov-26	20-Nov-26	**-35 CD**
L2E1070	Insulate and Hang Drywall - Level 2 East Wing	10d	23-Nov-26	08-Dec-26	**-39 CD**
L2E1080	Tape and Finish Drywall - Level 2 East Wing	10d	09-Dec-26	22-Dec-26	**-39 CD**
L2W1080	Tape and Finish Drywall - Level 2 West Wing	10d	23-Dec-26	11-Jan-27	**-41 CD**
L2W1090	Prime and First Coat Paint - Level 2 West Wing	6d	12-Jan-27	19-Jan-27	**-41 CD**
L2W1100	Install Ceiling Grid - Level 2 West Wing	6d	20-Jan-27	27-Jan-27	**-41 CD**
L2W1110	Above-Ceiling Inspection - Level 2 West Wing	2d	28-Jan-27	29-Jan-27	**-39 CD**
L2W1120	Install Ceiling Devices and Light Fixtures - Level 2 West Wing	8d	01-Feb-27	10-Feb-27	**-35 CD**
L2W1130	Install Ceiling Tile - Level 2 West Wing	5d	11-Feb-27	17-Feb-27	**-35 CD**
L2W1150	Install Resilient Flooring and Base - Level 2 West Wing	8d	18-Feb-27	01-Mar-27	**-35 CD**
L2W1160	Hang Doors and Install Hardware - Level 2 West Wing	6d	02-Mar-27	09-Mar-27	**-35 CD**
L2W1180	Final Paint and Touch-Up - Level 2 West Wing	4d	10-Mar-27	15-Mar-27	**-35 CD**
L2W1190	Final Clean and Punch List - Level 2 West Wing	5d	16-Mar-27	22-Mar-27	**-35 CD**
CL1000	Fire Alarm Acceptance Test	3d	23-Mar-27	25-Mar-27	**-35 CD**
CL1030	Fire Marshal Final Inspection	3d	26-Mar-27	30-Mar-27	**-35 CD**
MS1040	Substantial Completion	0d	30-Mar-27	30-Mar-27	**-35 CD**

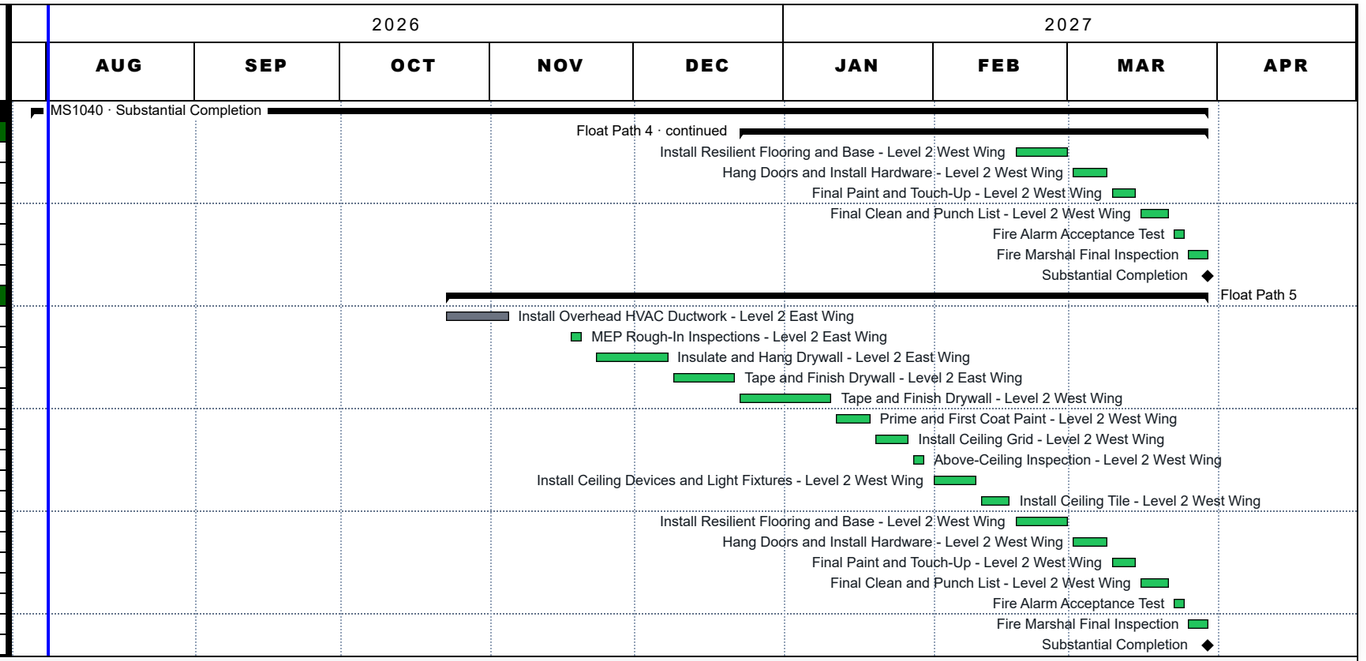

LEGEND

- Path 1
- Actual work
- Milestone
- Path 5
- Summary

Mountain Ridge Elementary School

Substantial Completion · Phase Path Report

ORGANIZATION	Sample Builders
DATA DATE	01-Aug-26
TURNOVER	Substantial Completion
LAYOUT	Phase Path Report
